

	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School

- Ⓡ Completed week ending Friday, July 16, 2021
 - Biweekly meeting on open commissioning items was held
 - Meeting took place with LS Black to review final outstanding costs.
 - Meeting to review Chiller Unit and roof screens took place.
- Ⓡ Planned week ending Friday, July 23, 2021
 - Continue financial and administration closeout

Centennial Elementary

- Ⓡ Completed week ending Friday, July 16, 2021
 - Continued commissioning of the chiller system.
- Ⓡ Planned week ending Friday, July 23, 2021
 - Contractor to address issues identified on the commissioning issues log.

Sheridan Hills Elementary

- Ⓡ Completed week ending Friday, July 16, 2021
 - Lower Level/Tunnels
 - Continued plumbing and hydronic piping installation.
 - Classroom Wings
 - Continued overhead electrical rough-in in the corridors.
 - Completed interior vestibule storefronts at the entrances.
 - Continued duct work installation in the B-wing classrooms and corridor.
 - Kitchen/Cafeteria/Receiving
 - Began underground plumbing in the Kitchen/Cafeteria.
 - Completed the new concrete slab in the Receiving addition.
 - Began installing the new built-up roofing
- Ⓡ Planned week ending Friday, July 23, 2021
 - Lower Level/Tunnels
 - Continue plumbing and hydronic piping installation.
 - Classroom Wings

	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Complete exterior storefronts install at the entrances.
- Continued overhead electrical rough-in in the corridors.
- Flooring contractor to mobilize and begin removing existing glue and mastic residue.
- Begin framing plumbing walls in the classrooms.
- Kitchen/Cafeteria/Receiving
 - Complete underground plumbing.
 - Begin concrete infills at underground plumbing trenches.

Middle School

Ⓡ Completed week ending Friday, July 16, 2021

- Front Entrance
 - Started painting
 - Installed unit heaters
- Cafeteria-Dishwashing Area
 - Finished underground plumbing
 - Poured back concrete floor
- Bathrooms
 - Start mechanical rough ins
- Corridors
 - Finished ceiling grid and light fixtures
- 2nd Level Breakout Room-3rd Level Classroom
 - Drywall framing on 2nd level breakout rooms
 - Mechanical and electrical rough in for 3rd level classroom
- Boiler Room
 - Installed doors and frames in boiler room
 - Continued to install boiler piping
- Best Buy Teen Tech Center-Music Suite-Educational Pathways
 - Demolition
 - Wall and window framing

Ⓡ Planned week ending Friday, July 23, 2021

- Front Entrance
 - Start installing ceiling grid
 - Continue painting
 - Start installing storefront

	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Cafeteria-Dishwashing Area
 - Install floor tile
- Bathrooms
 - Wall framing
- 2nd Level Breakout Room-3rd Level Classroom
 - Tape, mud, drywall finishes in breakout rooms
 - Finish mechanical and electrical rough in at 3rd level classroom
- Boiler Room
 - Continue to install boiler, water heater, and pump piping
- Best Buy Teen Tech Center-Music Suite-Educational Pathways
 - In wall mechanical and electrical rough ins

STEM

- Ⓡ Completed week ending Friday, July 16, 2021
 - Continued commissioning of chiller/cooling system took place
- Ⓡ Planned week ending Friday, July 23, 2021
 - Continue commissioning of chiller/cooling system

Central Ed.

- Ⓡ Completed week ending Friday, July 16, 2021
 - Administration Spaces and Area D Offices
 - Continued finned tube radiation install.
 - Classroom Wings
 - Began wall framing in the classrooms and toilet rooms.
 - Began prepping floors and walls for tile installation.
 - Sitework/Chiller Enclosure/Mech Spaces
 - Completed footings and foundations at the Chiller enclosure.
 - Began backfilling at the chiller enclosure and prep work for new sidewalk.
- Ⓡ Planned week ending Friday, Jul 23, 2021
 - Administration Spaces and Area D Offices
 - Complete acoustical ceiling tiles.
 - Complete flooring installation.

	ICS Weekly Project Report July 16, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423


- Classroom Wings
 - Continue mechanical and electrical rough-in.
 - Begin creating roof openings for new mechanical equipment.
 - Begin taping and sanding drywall.
 - Begin tile work in the Toilet rooms.
- Sitework/Chiller Enclosure
 - Finish prepping and pour new sidewalks.

	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

CURRENT PROJECT PHOTOS
Middle School – Educational Pathways Window and Wall Framing



Middle School – Best Buy Teen Tech Center and Music Suite Wall Framing

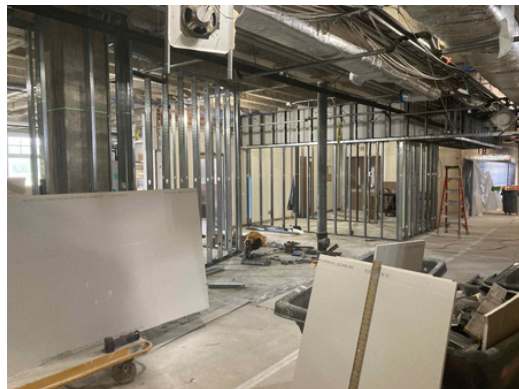


	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Cafeteria Entrance Drywall Framing



Middle School – Dishwasher Concrete Floor Poured Back In

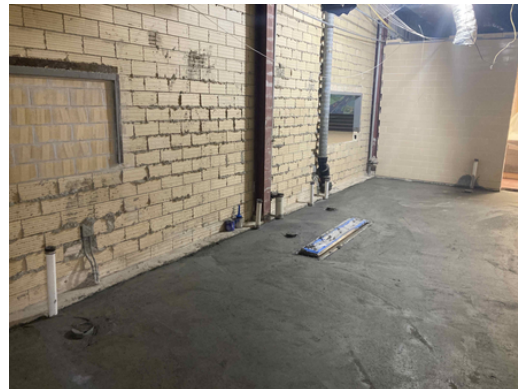

Middle School – Second Level Breakout Rooms Drywall Framing



	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills –Poured concrete slab in the Receiving addition.



Sheridan Hills – Underground plumbing in the Kitchen.



Sheridan Hills – Duct work and unit ventilator installation in the classrooms.



	ICS Weekly Project Report July 16, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Central Ed. – Metal stud wall framing in the classrooms and Toilet rooms.



Central Ed. – Concrete footings and foundation wall formwork at the Chiller enclosure.



Central Ed. – Mirrors installed in Activity Center. Drywall installation in the classrooms.

