

	ICS Weekly Project Report September 10, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills Elementary

Ⓡ Completed week ending Friday, September 10, 2021

- Kitchen/Cafeteria/Receiving
 - Cafeteria passed final inspections and is now being used for dining.
 - Kitchen equipment is being installed and final mechanical and electrical connections are being made.
 - Plumbing fixtures and specialties were installed in the Receiving area Toilet room.
 - Flooring was installed in the Food Service office.
 - Completed roof parapet metal coping.
- Site
 - Continued site clean-up and demobilization.
 - Place concrete for stairs at Gym exit tentatively planned for Saturday 9/11.

Ⓡ Planned week ending Friday, September 17, 2021

- Kitchen/Cafeteria/Receiving
 - Complete all remaining work in the Kitchen.
 - Final cleaning in the Kitchen.
 - Conduct all required City and State (Health Department) inspections to allow for full occupancy of the Kitchen.
- Site
 - Continue site clean-up and demobilization.
- General
 - Resume testing and balancing of the HVAC system.
 - Contactors to address punchlist items.

Middle School

Ⓡ Completed week ending Friday, September 10, 2021

- Main Entrance
 - Card readers and push button entrances installed
- Bathrooms
 - Installed toilet partitions
- Boiler Room
 - Scheduled start up and training for September 20th

	ICS Weekly Project Report September 10, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Best Buy Teen Tech Center
 - Floor covering installed
- Continued auditorium HVAC hydronic re-piping

Ⓡ Planned week ending Friday, September 17, 2021

- Bathrooms
 - Install backordered floor tile, wait for remaining wall tile
- Best Buy Teen Tech Center
 - Waiting on shipment of doors week of 9/20
- Finish auditorium HVAC hydronic re-piping and clear out auditorium foyer

Central

Ⓡ Completed week ending Friday, September 10, 2021

- Classroom Wings
 - Completed wall and door frame painting in the 300 wing offices.
 - Completed flooring and base in the 300 wing offices.
 - Completed all work in the multi-user toilet rooms in the 300 and 400 wings.
 - Wold continued conducting punchlist walkthroughs of finished spaces.
- Mech Spaces
 - Continued chilled water piping and connections to mech equipment.
 - Continued installing rooftop ductwork.
- General
 - Contractor continued general clean-up and demobilization in and around the building.
 - All-State is in the process of programming the security and intrusions systems.

Ⓡ Planned week ending Friday, September 17, 2021

- Mech Spaces
 - Contractors to continue completing work associated with the building cooling system in preparation for systems start-up on 9/23.
 - Continue rooftop ductwork and exhaust fans installation.
- General
 - Complete dishwasher and sink installation the Prep Room.
 - Contractors to work to address punchlist items.

	ICS Weekly Project Report September 10, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

CURRENT PROJECT PHOTOS

Middle School – Loading Dock Bathrooms Toilet Partitions Installed



Middle School – Best Buy Teen Tech Center Carpet Installed



Sheridan Hills – Cafeteria set-up for student dining.




	ICS Weekly Project Report September 10, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423



Sheridan Hills – Kitchen equipment installation in-progress.



Sheridan Hills – Receiving addition parapet coping completed. Receiving area interior painting completed.

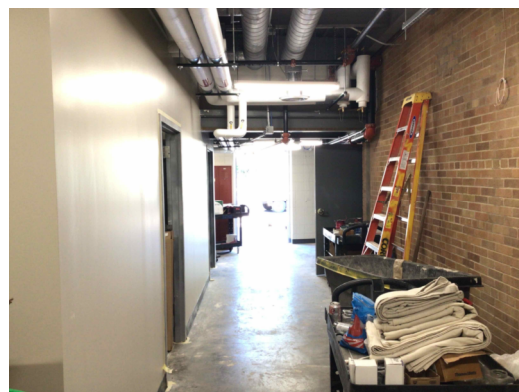

Central Ed. – Completed Toilet room.

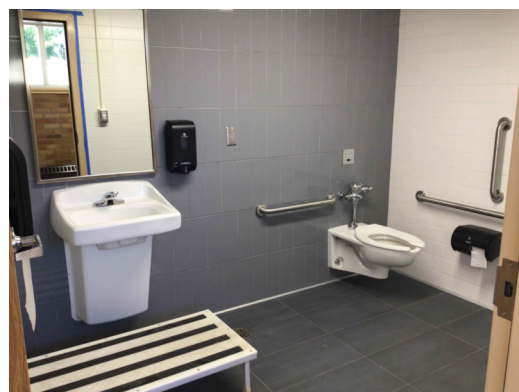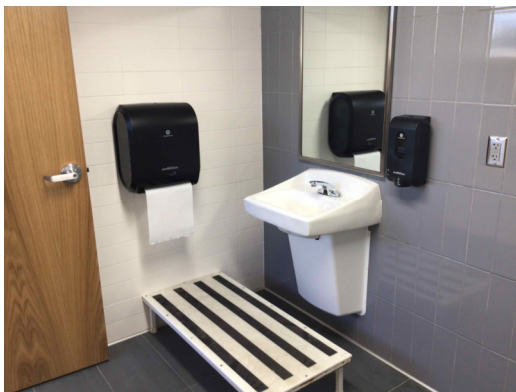

	ICS Weekly Project Report September 10, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Central Ed. – 300 wing offices completed.



Central Ed. – Chiller unit piping and final connections. Rooftop ductwork and exhaust fan installation.



Central Ed. – Multi-purpose Room and Gym cleared of construction materials and cleaned.

